Project 801

Ferguson Marine

AC 684

REV 1

Updated	18-Jan-24
Project Start:	Mon, 01/01/2024
Display Week:	3

SIMPLE GANTT CHART by Vertex42.com

https://www.vertex42.com/ExcelTemplates/simple-gantt-chart.html

CRITICAL

TASK	ASSIGNED TO	PROGRESS	START	END	DAYS	DAYS
NAVAGATION & SAFETY						
Evacuation Plan & Signs		70%	5-Jan-24	5-Feb-24	32	
Muster Plans		70%	5-Jan-24	5-Feb-24	32	
Operational Manuals		80%	5-Jan-24	5-Feb-24	32	
Integrated Bridge Training		40%	5-Jan-24	18-Jan-24	14	
Radio Survey		80%	5-Jan-24	19-Jan-24	15	
LSA Equipment		50%	5-Jan-24	9-Feb-24	36	
Radio Survey		95%	15-Jan-24	16-Jan-24	2	
Inclining Pre-Sea Trials		60%	9-Feb-24	10-Feb-24	2	
Fire Insulation		60%	5-Jan-24	10-Feb-24	37	
Installation LSA Equipment		60%	5-Jan-24	5-Feb-24	32	
MECHANICAL & OUTFIT						
Fuel Oil Systems Operational		100%	5-Jan-24	15-Jan-24	11	11
Lub Oil Systems Operational		100%	5-Jan-24	15-Jan-24	11	11
Cooling Systems Operational		100%	5-Jan-24	15-Jan-24	11	11
Compressed Air Sytems Operational		100%	5-Jan-24	15-Jan-24	11	11
Exhaust Systems Operational		100%	5-Jan-24	15-Jan-24	11	11
Bilhge Systems Operational		100%	5-Jan-24	15-Jan-24	11	11
Fire Fighting System Operational		80%	5-Jan-24	12-Feb-24	39	39
Local Fire Fighting System		60%	5-Jan-24	6-Feb-24	33	33
Fire Detection Operational		70%	5-Jan-24	12-Feb-24	39	39
Inclining Pre-Sea Trials		0%	9-Feb-24	10-Feb-24	2	2
Pre-Sea Trials Dock Trials		0%	10-Feb-24	12-Feb-24	3	3
Life Raft Hire &Installation		60%	29-Jan-24	5-Feb-24	8	
Dmestic Fresh Water System		80%	5-Jan-24	22-Jan-24	18	
Sewage System		70%	29-Jan-24	5-Feb-24	8	
Galley Outfit		90%	5-Jan-24	5-Feb-24	32	
Accommodation trials support		85%	5-Jan-24	5-Feb-24	32	
FRC Installation & Test		90%	5-Jan-24	15-Jan-24	11	11
Crew Training		90%	5-Jan-24	15-Jan-24	11	11
Sea Trials Exemption Certificate						
Trials Exemption Certificate		0%	12-Feb-24	12-Feb-24	1	1

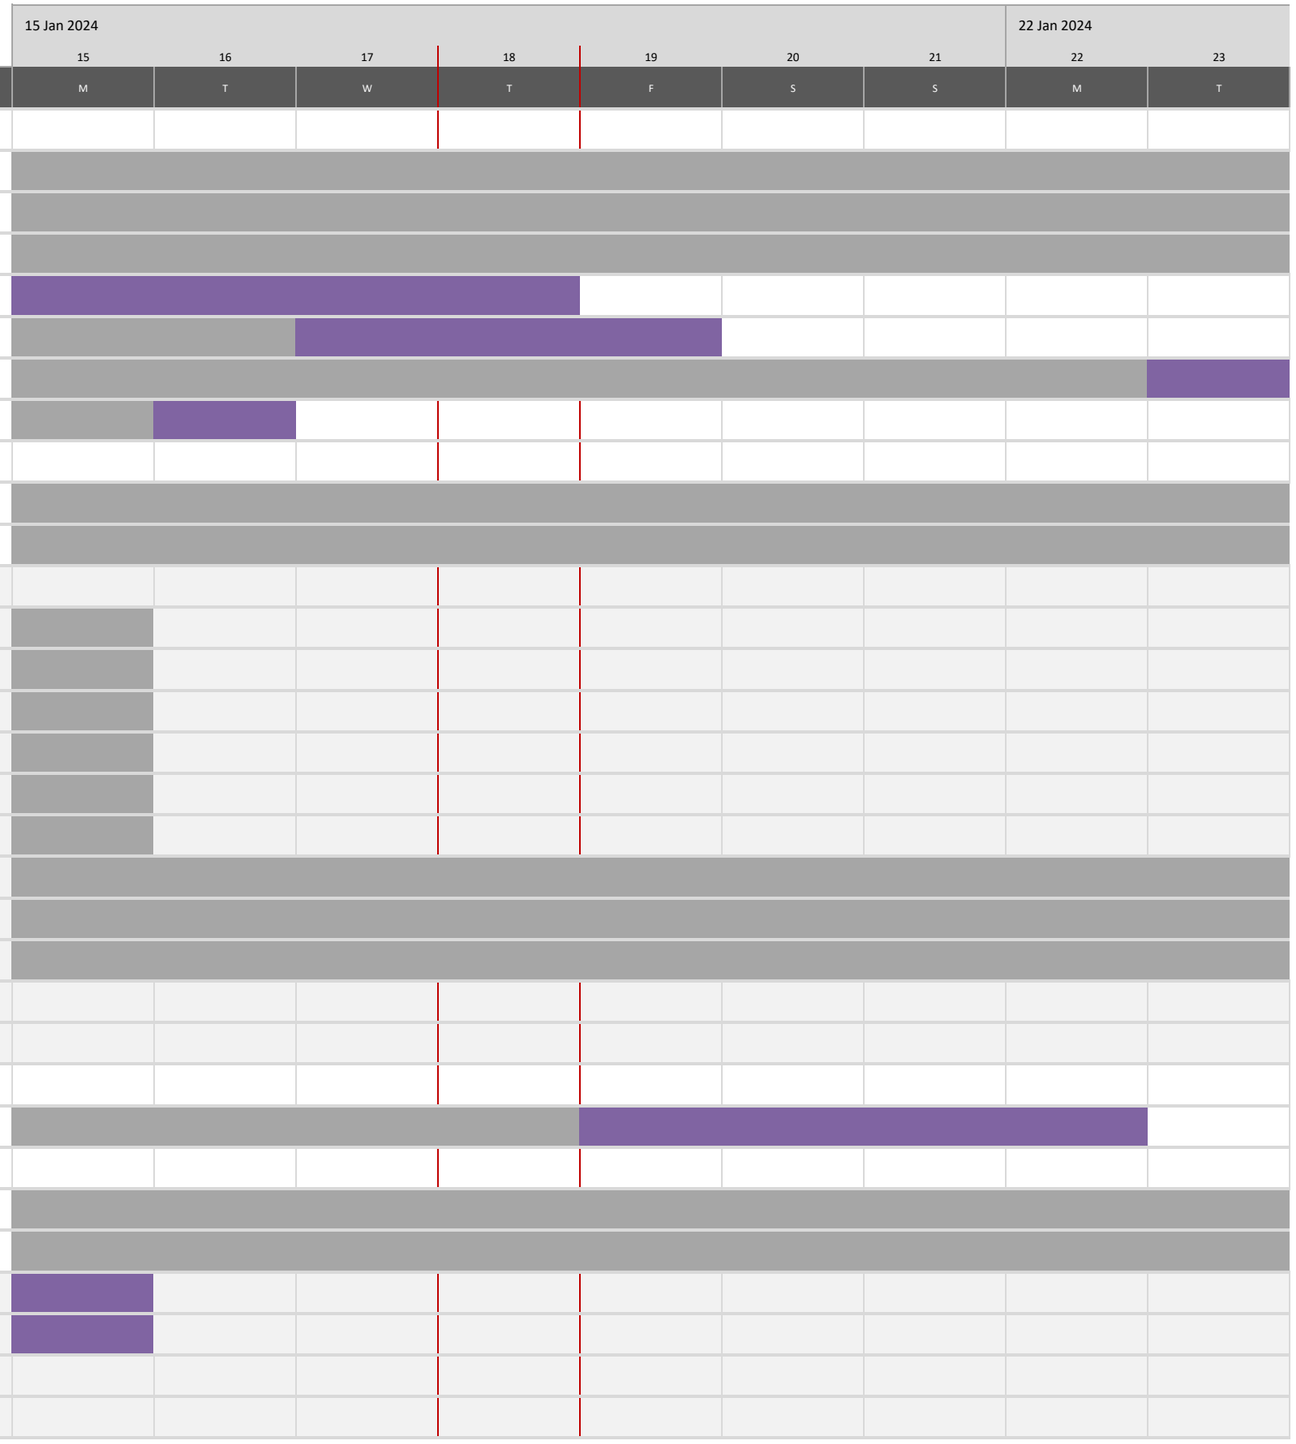

GLEN SANNOX

. PATH TO (MGO) BUILDERS TRIALS

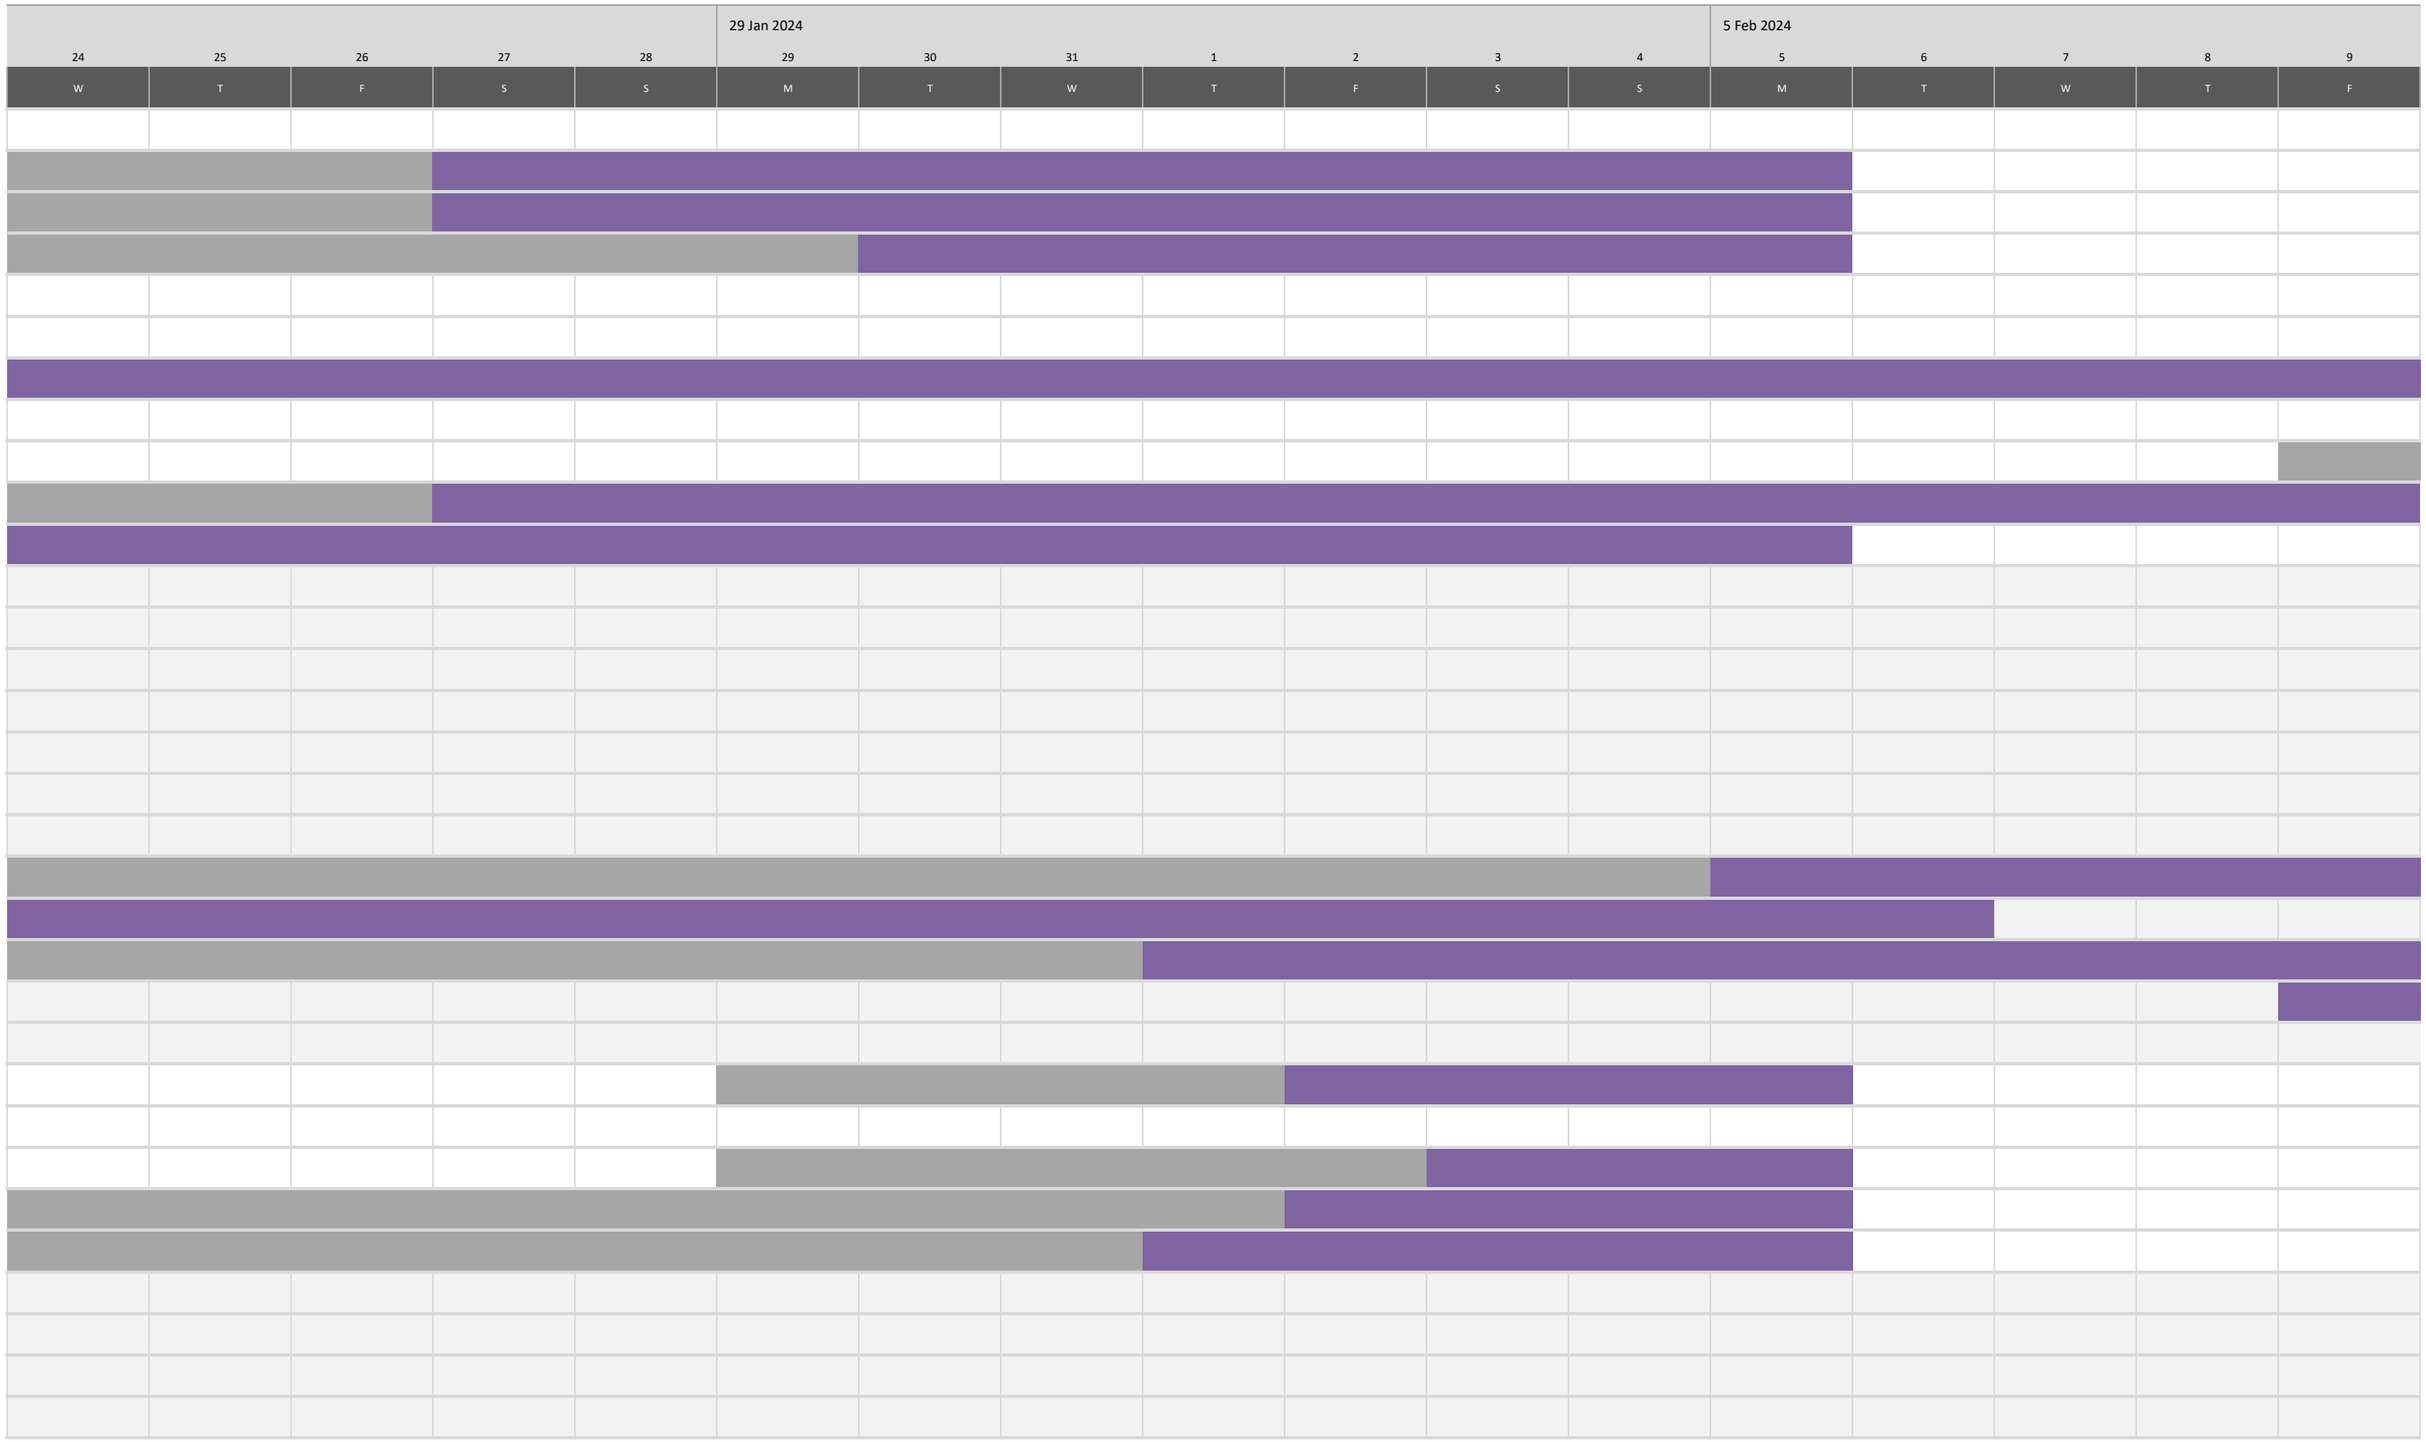

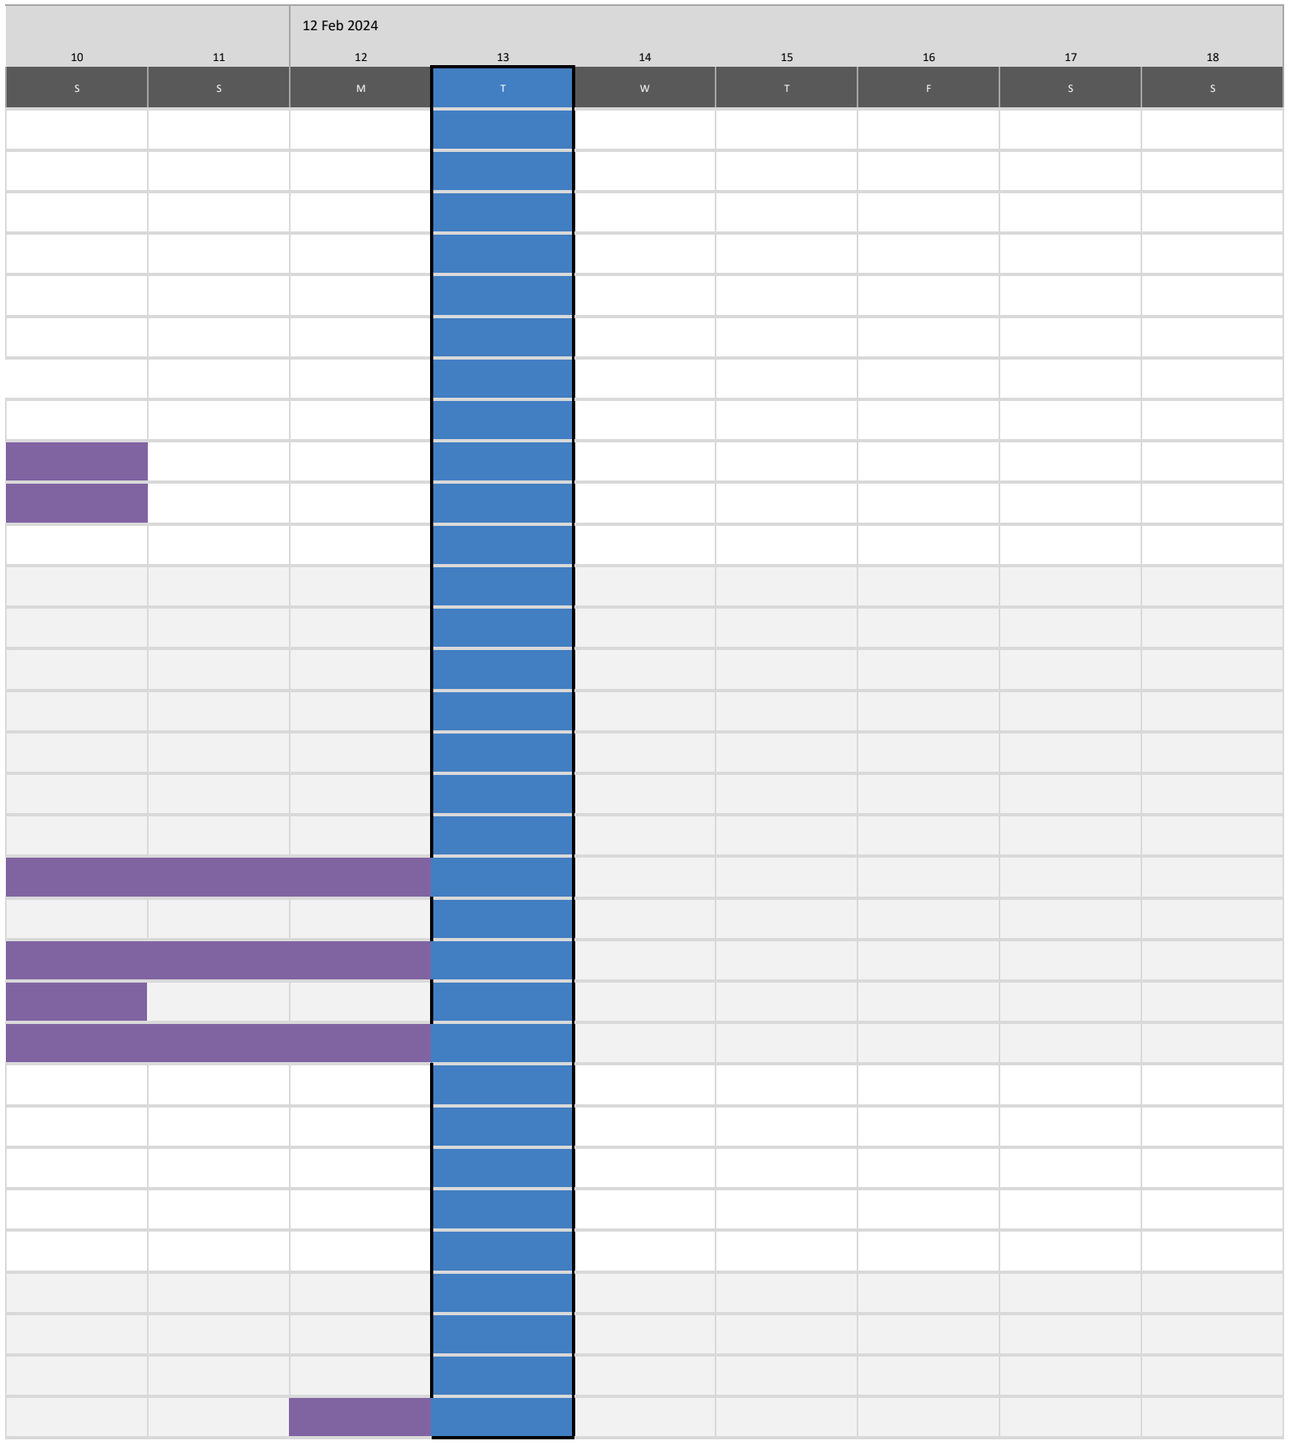
12 Feb 2024
10
11
12
13
14
15
16
17
18
S
S
M
T
W
T
F
S
S
